




Detail Gradation Statistical Summary Report

Plant 02-Hudson Mine
Product 2 B-Hudson Concrete Sand
Specification Hudson Concrete Sand
Period 04/01/2025 - 04/30/2025

Sieve/Test	Tests	Average	Min	Max	Range	St Dev	Target	Specification	PWS
3/8" (9.5mm)	22	100.0	100.0	100.0	0.0	0.00		100-100	100.0
#4 (4.75mm)	22	99.7	99.4	99.8	0.4	0.13		95-100	100.0
#8 (2.36mm)	22	97.3	96.3	98.2	1.9	0.47			
#16 (1.18mm)	22	84.8	82.3	88.3	6.0	1.45		45-95	100.0
#30 (.6mm)	22	50.0	40.9	58.0	17.1	3.58			
#50 (.3mm)	22	15.2	12.4	19.3	6.9	1.83		5-30	100.0
#100 (.15mm)	22	2.1	1.4	3.2	1.8	0.57		0-10	100.0
Pan	22	0.00	0.00	0.00	0.00	0.000		0-3	100.0
FM	22	2.510	2.334	2.637	0.303	0.0662			
SE	4	91.250	89.000	94.000	5.000	2.2174			
Wash Loss (#200/75um)	4	0.476	0.395	0.550	0.155	0.0656			

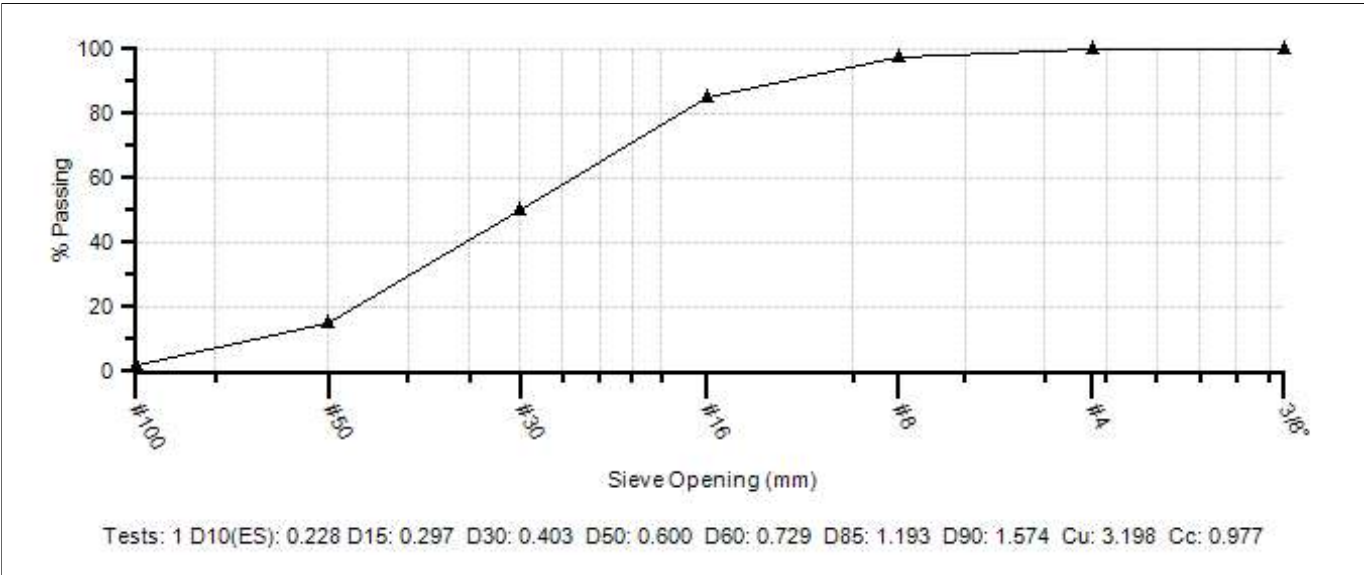

Comments

Query

Query Selections
Date Created 05/01/2025
Date Range 04/01/2025 - 04/30/2025
Plant Hudson Mine
