


Detail Gradation Statistical Summary Report

Plant 02-Hudson Mine
Product 2 B-Hudson Concrete Sand
Specification Hudson Concrete Sand
Period 04/01/2026 - 04/30/2026

Sieve/Test	Tests	Average	Min	Max	Range	St Dev	Target	Specification	PWS
3/8" (9.5mm)	22	100.0	100.0	100.0	0.0	0.00		100-100	100.0
#4 (4.75mm)	22	99.6	99.2	99.9	0.7	0.21		95-100	100.0
#8 (2.36mm)	22	97.3	95.4	98.5	3.1	0.76			
#16 (1.18mm)	22	85.2	79.9	89.6	9.7	2.81		45-95	100.0
#30 (.6mm)	22	51.9	34.9	62.2	27.3	6.15			
#50 (.3mm)	22	16.6	6.7	25.2	18.5	3.67		5-30	99.9
#100 (.15mm)	22	2.0	1.0	4.5	3.5	0.78		0-10	100.0
Pan	22	0.00	0.00	0.00	0.00	0.000		0-3	100.0
FM	22	2.474	2.219	2.778	0.559	0.1284			
SE	5	90.200	89.000	92.000	3.000	1.3038			
Wash Loss (#200/75um)	5	0.515	0.411	0.610	0.199	0.0903			

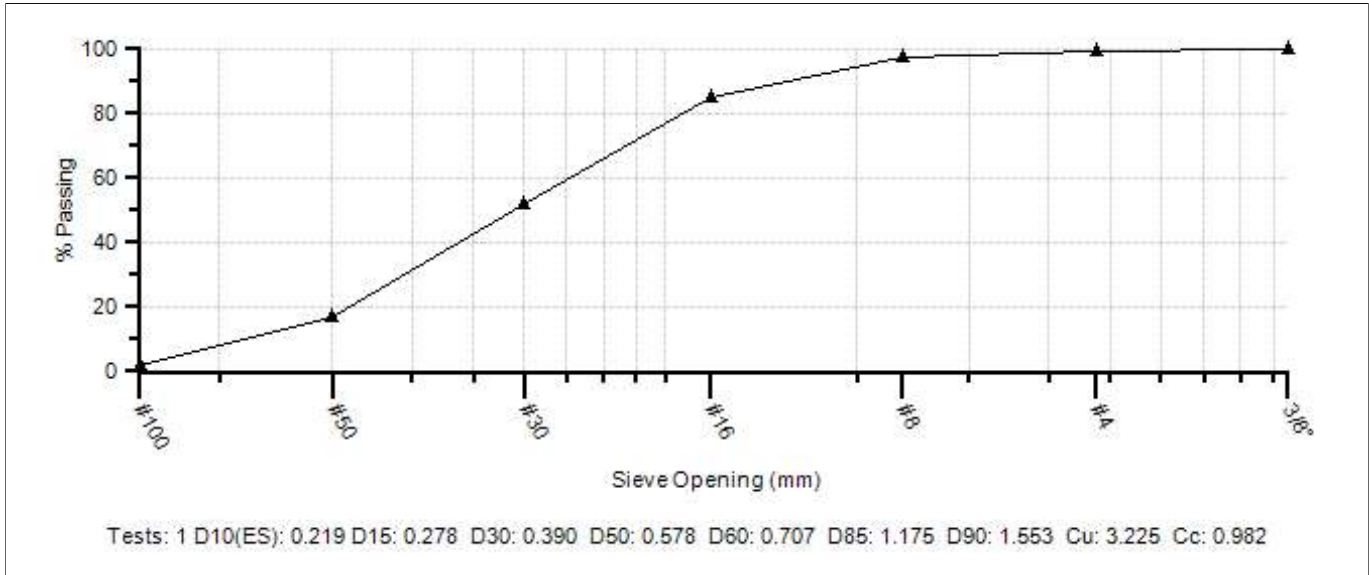

Comments

Query

Query Selections
Date Created 05/01/2026
Date Range 04/01/2026 - 04/30/2026
Plant Hudson Mine
Sample Type Shipping
Sample Method Load-Out Face
