


## Detail Gradation Statistical Summary Report

**Plant** 03-Fort Gordon Plant  
**Product** 2A-Fort Gordon Concrete Sand  
**Specification** Fort Gordon Concrete Sand  
**Period** 05/01/2026 - 05/31/2026

Sieve/Test	Tests	Average	Min	Max	Range	St Dev	Target	Specification	PWS
3/8" (9.5mm)	20	100.0	100.0	100.0	0.0	0.00		100-100	100.0
#4 (4.75mm)	20	99.6	99.3	99.9	0.6	0.17		95-100	100.0
#8 (2.36mm)	20	97.5	96.5	98.5	2.0	0.54			
#16 (1.18mm)	20	87.8	84.3	94.0	9.7	2.43		45-95	99.8
#30 (.6mm)	20	47.7	41.9	62.1	20.2	5.50			
#50 (.3mm)	20	11.3	8.4	14.3	5.9	1.83		5-30	100.0
#100 (.15mm)	20	0.4	0.0	0.8	0.8	0.37		0-10	100.0
Pan	20	0.00	0.00	0.00	0.00	0.000			
FM	20	2.558	2.340	2.678	0.338	0.0967			
SE	5	86.800	82.000	94.000	12.000	5.7619			
Wash Loss (#200/75um)	4	0.688	0.380	0.976	0.596	0.2511			

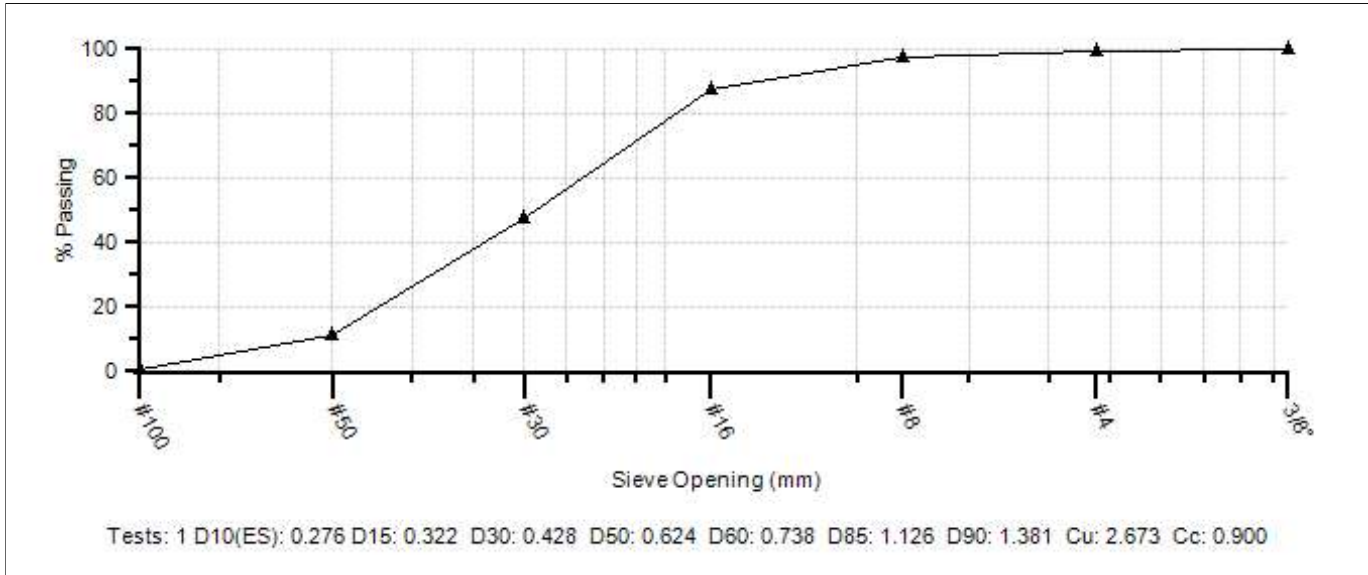

**Comments**

**Query**

Query Selections  
Date Created 06/05/2026  
Date Range 05/01/2026 - 05/31/2026  
Plant Fort Gordon Plant  
Sample Type Shipping  
Sample Method Load-Out Face
