


Detail Gradation Statistical Summary Report

Plant 03-Fort Gordon Plant
Product 2A-Fort Gordon Concrete Sand
Specification Fort Gordon Concrete Sand
Period 06/01/2026 - 06/30/2026

Sieve/Test	Tests	Average	Min	Max	Range	St Dev	Target	Specification	PWS
3/8" (9.5mm)	23	100.0	100.0	100.0	0.0	0.00		100-100	100.0
#4 (4.75mm)	23	99.6	99.2	99.9	0.7	0.20		95-100	100.0
#8 (2.36mm)	23	98.0	97.1	98.9	1.8	0.48			
#16 (1.18mm)	23	89.6	84.5	93.8	9.3	2.47		45-95	98.6
#30 (.6mm)	23	51.4	39.1	61.1	22.0	6.09			
#50 (.3mm)	23	12.5	9.0	14.6	5.6	1.70		5-30	100.0
#100 (.15mm)	23	0.4	0.0	0.8	0.8	0.30		0-10	100.0
Pan	23	0.00	0.00	0.00	0.00	0.000			
FM	23	2.484	2.322	2.685	0.363	0.1018			
SE	5	84.000	80.000	90.000	10.000	3.9370			
Wash Loss (#200/75um)	5	0.582	0.422	0.813	0.391	0.1732			

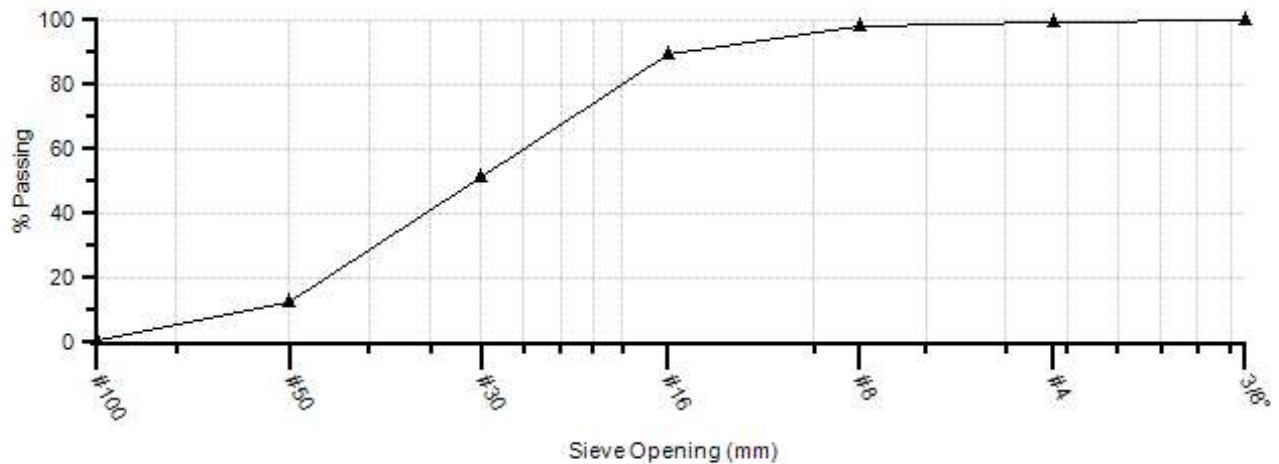

Tests: 1 D10(ES): 0.260 D15: 0.314 D30: 0.410 D50: 0.585 D60: 0.699 D85: 1.088 D90: 1.220 Cu: 2.688 Cc: 0.924

Comments**Query**

Query Selections

Date Created 07/06/2026

Date Range 06/01/2026 - 06/30/2026

Plant Fort Gordon Plant

Sample Type Shipping

Sample Method Load-Out Face
